Delivery 1 - Load 1 of 2 - 18 t rigid

7 pallets in 3 of 3 floor positions | 143 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

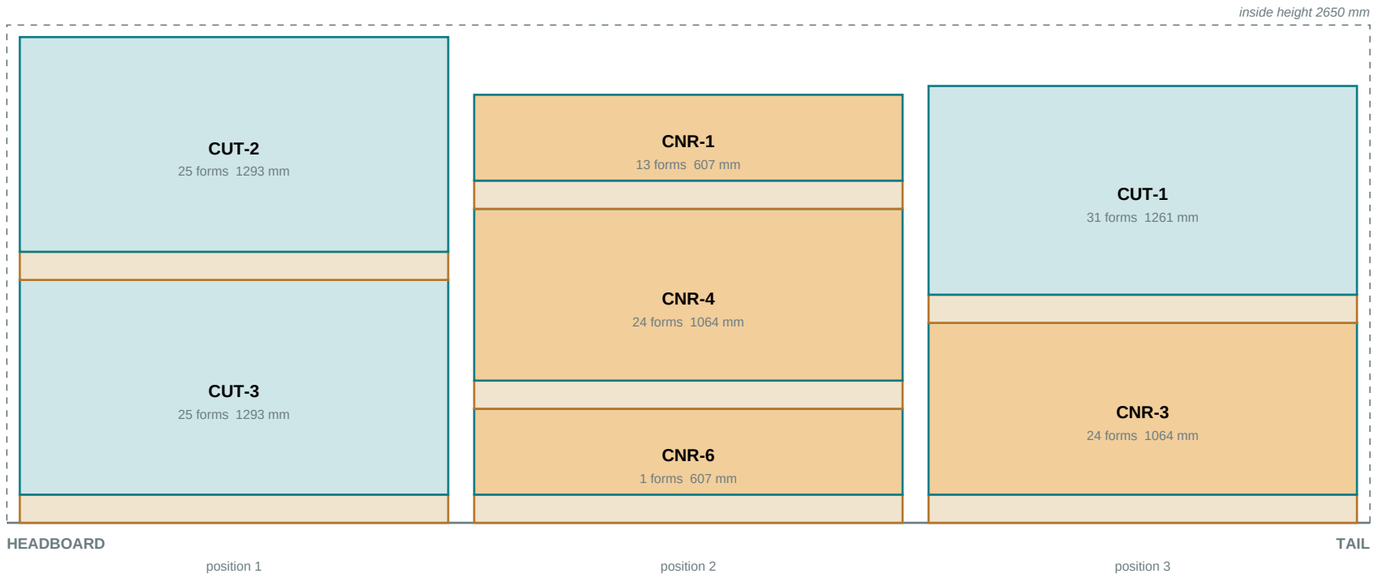

Unload order - 6 of 6 pallets come off out of build order, the price of stacking tallest forward

1. CUT-1 8in Std straights 31 forms courses FB course 1
2. CNR-3 6in XR35 corners 24 forms courses L1 courses 2-4
3. CNR-1 8in Std corners 13 forms courses FB course 1
4. CNR-4 6in XR35 corners 24 forms courses L1 courses 4-6
5. CNR-6 6in XR35 corners 1 forms courses L1 course 8
6. CUT-2 6in XR35 straights 25 forms courses L1 courses 1-7
7. CUT-3 6in XR35 straights 25 forms courses L1 courses 1-8

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-063 Ethos Property Development - Lan…	FORMS	143
VEHICLE	18 t rigid	POSITIONS	3 of 3
PALLETS	7	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - 18 t rigid

6 pallets in 3 of 3 floor positions | 145 forms | tallest column 2586 mm of 2650 mm inside height

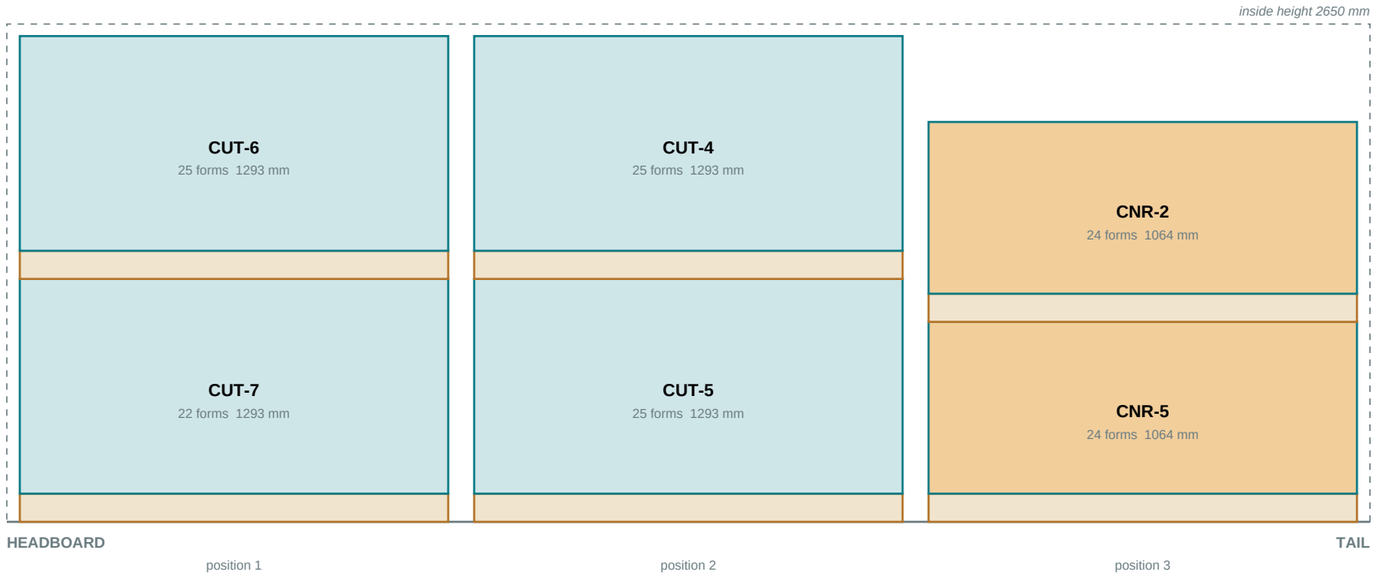

Unload order - 5 of 5 pallets come off out of build order, the price of stacking tallest forward

1. CNR-2 6in XR35 corners 24 forms courses L1 courses 1-2
2. CNR-5 6in XR35 corners 24 forms courses L1 courses 6-8
3. CUT-4 6in XR35 straights 25 forms courses L1 courses 2-7
4. CUT-5 6in XR35 straights 25 forms courses L1 courses 3-7
5. CUT-6 6in XR35 straights 25 forms courses L1 courses 5-7
6. CUT-7 6in XR35 straights 22 forms courses L1 courses 7-8

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-063 Ethos Property Development - Lan…	FORMS	145
VEHICLE	18 t rigid	POSITIONS	3 of 3
PALLETS	6	TALLEST	2586 mm

Delivery 2 - Load 1 of 1 - 18 t rigid

4 pallets in 2 of 3 floor positions | 64 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

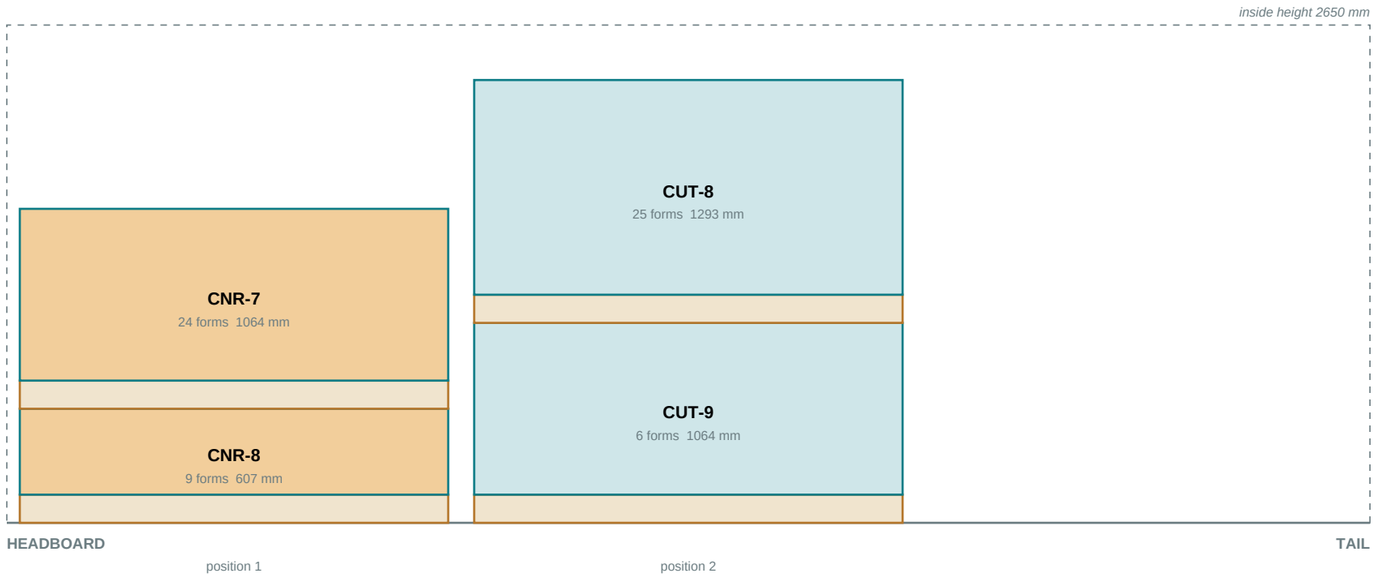

Unload order - 3 of 3 pallets come off out of build order, the price of stacking tallest forward

1. CUT-8 6in XR35 straights 25 forms courses L2 courses 1-7
2. CUT-9 6in XR35 straights 6 forms courses L2 courses 3-7
3. CNR-7 6in XR35 corners 24 forms courses L2 courses 1-5
4. CNR-8 6in XR35 corners 9 forms courses L2 courses 5-7

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-063 Ethos Property Development - Lan…	FORMS	64
VEHICLE	18 t rigid	POSITIONS	2 of 3
PALLETS	4	TALLEST	2357 mm
